

NAIP 03

Lessons Learned

John Mootz
Contract Specialist


Communication

- Who does NAIP marketing?
- Customers don't know what is going on (poor dissemination of information)
- APFO could benefit from a better project tracking system

Flight Planning

- APFO had a duplicate count for a handful of QQs
- Don't cut coverage short along shorelines
- Expand the flying season to allow more clear weather days

**EXPECTANCY OF CLEAR AIR DAYS
EASTERN US**

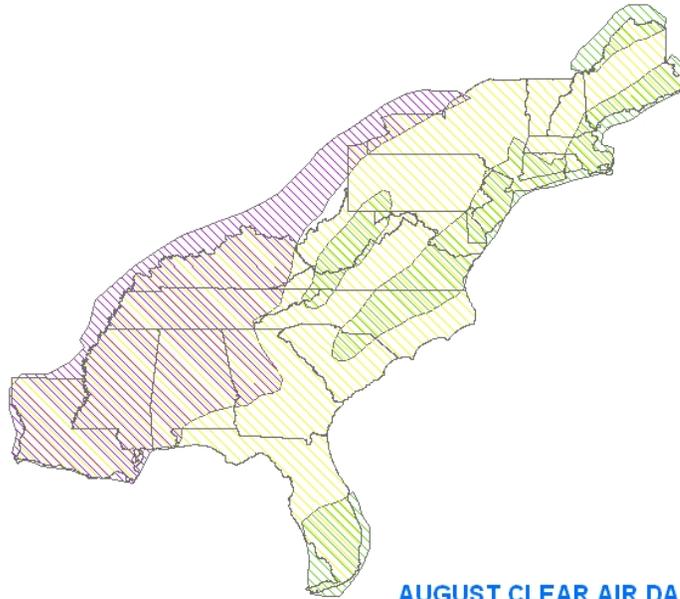


AUGUST CLEAR AIR DAYS

- 1-3 DAYS
- 3-6 DAYS
- 6-8 DAYS

Contract Performance

- Eliminate small-format digital camera
- Require vendor to color & tone balance
- Require incremental delivery of material
- Require accuracy statistical reports from vendor when tiles are delivered

Small-Format Digital Camera

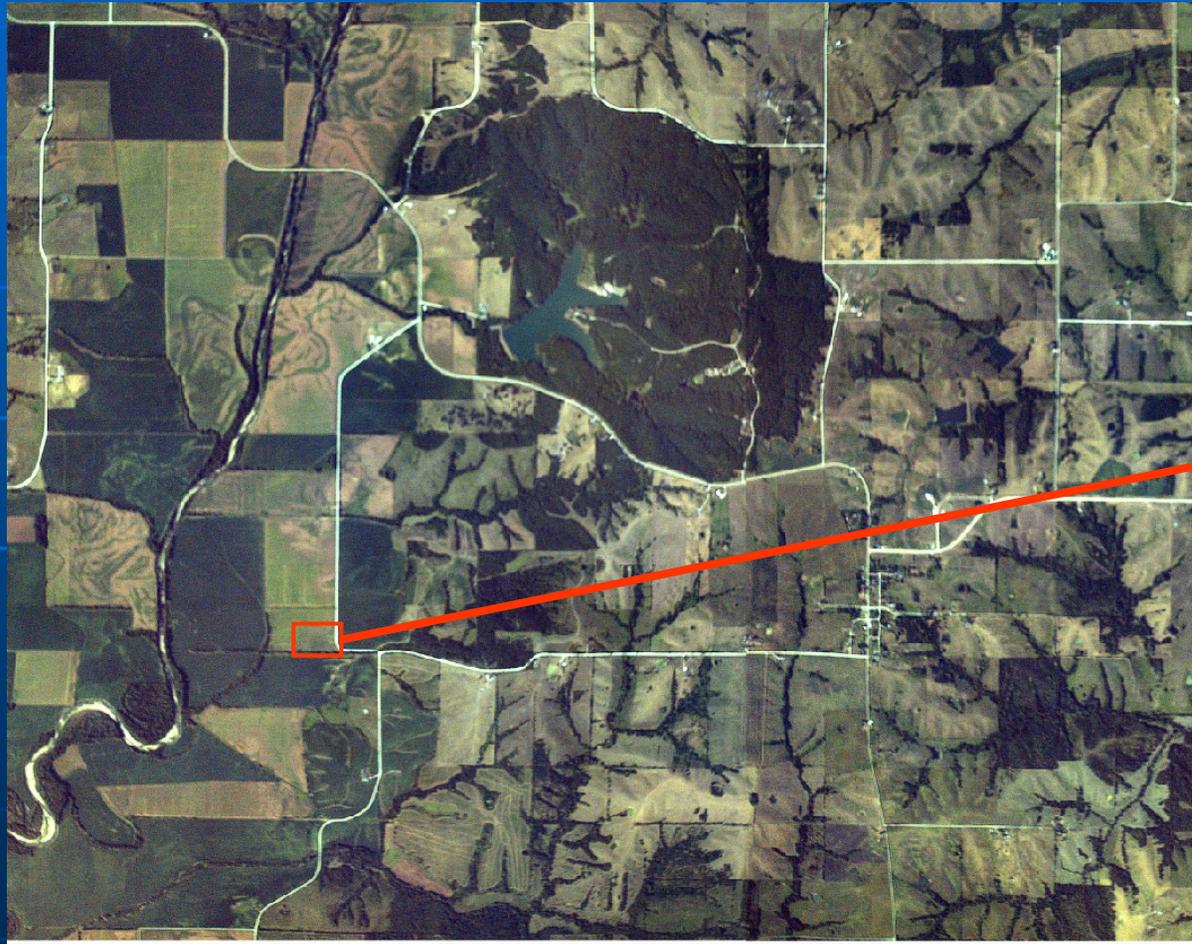

IT Support

- Storage capacity (inefficient use of tape library)
- Data ingestion (slow loading of tapes)
- Media formatting problems

Other Issues

- Standardize data format (GeoTiff, tiffWorld)
- Compression software
- APFO's capacity for inspection (slow work flow and thru-put)
